
SUPPLY SCOPE: Nudura ICF forms, accessories, pre-cut service, alignment hire and haulage as the quotation. ENGLAND - Building Regulations (LABC). 3rd-floor FFL ~8.23 m above the ground floor, below 11 m. 4 storeys incl. the attic (LABC warranty cap 3 - provider to confirm); Class 2A ties by the engineer. Precast floors, steels / transfer beams, roof structure, windows and timber partitions are shown in good faith for coordination only - engineer / specialists to design.

QUOTATION - NOT FOR CONSTRUCTION

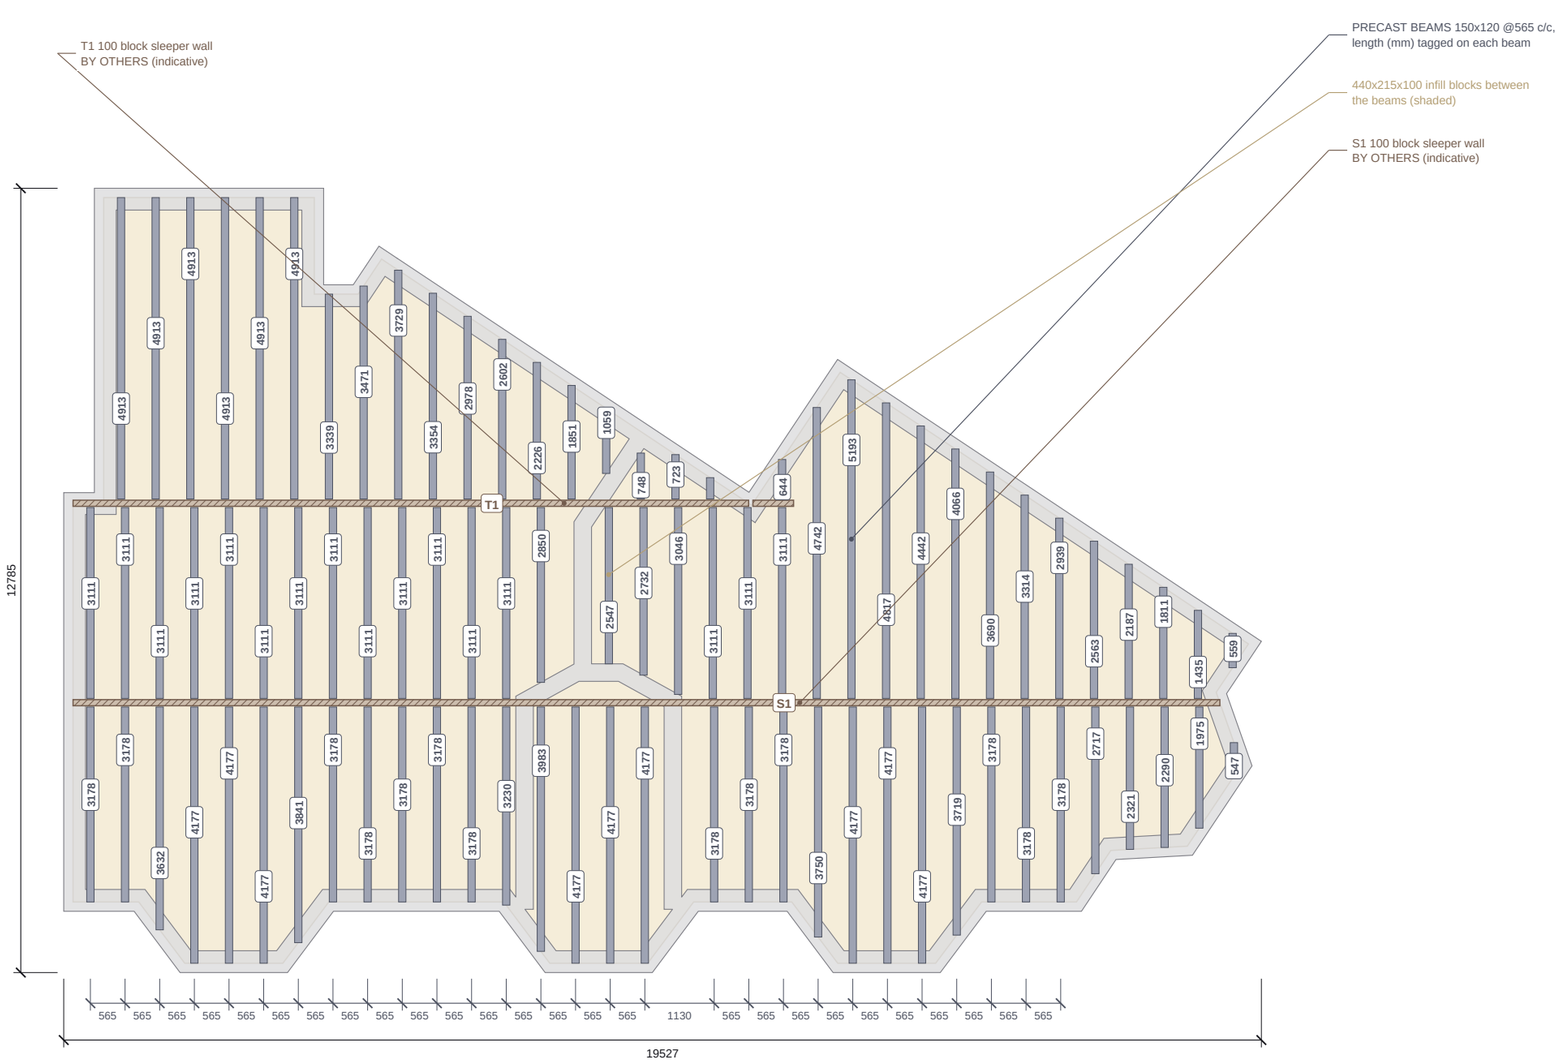

SOUTH (Bromfelde Road front)

Precast beam 150x120 | Infill block zone (floor outline) | ICF walls below (bearing) | Sleeper wall by others

GROUND FLOOR PRECAST BEAM AND BLOCK LAYOUT

Scale 1:100 @ A3 | Plan on the beams, screed / topping omitted. Walls below cut at -500

0 1 2 3 4 5m

Do not scale. All dimensions in mm. Check all dimensions on site.

GROUND FLOOR SCHEDULES

FLOOR BUILD-UP

Layer	mm	Underside / level
FFL (top of screed)	-	+0.0
Screed	50	-50
Rigid insulation	150	-200
Precast beam 150x120 + 100 infill	150	-350

FLOOR SUMMARY

Item	Qty
Floor area (m2)	161.9
Precast beams 150x120 @565 (No.)	85
Beam run (m)	270.2
Infill blocks 440x215x100 (No., +5%)	1,400
Max clear span (mm)	4,993
Insulation 150 + screed 50 (m2)	161.9

Infill = floor area / (0.565 x 0.215) + 5%, indicative - supplier to confirm.

STEELS / SLEEPER WALLS (INDICATIVE - ENGINEER)

Mark	Section	Line	Length	kg
S1	100 block sleeper (others)	y 3,400	18,698	-
T1	100 block sleeper (others)	y 6,651	11,015	-
T1	100 block sleeper (others)	y 6,651	663	-

BEAM SCHEDULE (LENGTH / QTY)

Length	Qty
<= 5,200	1
<= 5,000	6
<= 4,900	1
<= 4,800	1
<= 4,500	1
<= 4,200	9
<= 4,100	1
<= 4,000	1
<= 3,900	1
<= 3,800	3
<= 3,700	2
<= 3,500	1
<= 3,400	3
<= 3,300	1
<= 3,200	29
<= 3,100	1
<= 3,000	2

Length	Qty
<= 2,900	1
<= 2,800	2
<= 2,700	1
<= 2,600	2
<= 2,400	1
<= 2,300	2
<= 2,200	1
<= 2,000	1
<= 1,900	2
<= 1,500	1
<= 1,100	1
<= 800	2
<= 700	1
<= 600	2
<= 400	1
Total	85

Banded to the next 100 mm (overall incl. bearings); exact lengths tagged on the plan.

NOTES

1. Ground floor FFL +0.0: 50 screed on 150 rigid insulation on 150 precast beams (120 wide) @565 c/c + 440x215x100 infill blocks; beam top -200, soffit -350. Suspended over a ventilated void (depth / vents / DPM to the supplier and Building Regulations).
2. Beams bear on the ICF core of the walls below (grey, cut at -500) - minimum bearing, end details and any ties to the precast supplier. 85 beams, 270.2 m; max clear span 4,993 (none over 5 m).
3. GF SLEEPER WALLS S1 / T1: 100 blockwork on footings BY OTHERS (intermediate beam bearings, under the 1F steel lines) - indicative, engineer / groundworker to confirm.
4. Precast supplier to design and confirm the beams, infill, bearings and layout; drawn for pricing / coordination only. Levels above GF FFL, mm.

REVISIONS

REV	DATE	DESCRIPTION
-	02.11.26	Quotation issue

Nudura™ BuildEase

CLIENT	PROJECT
JAUS (via Tremco CPG UK)	Bromfelde Corner, 25 Bromfelde Road, London SW4 6PP

DRAWING TITLE

GROUND FLOOR STRUCTURE

Precast beam and block layout, beam lengths, steels, voids

SCALE	SIZE	DATE
1:100	A3	02.11.26
DRAWN	CHECKED	APPROVED
TS		

STATUS	DRAWING No.	REV
QUOTATION	ES26-087-FL-01	-
