Delivery 1 - Load 1 of 2 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 225 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

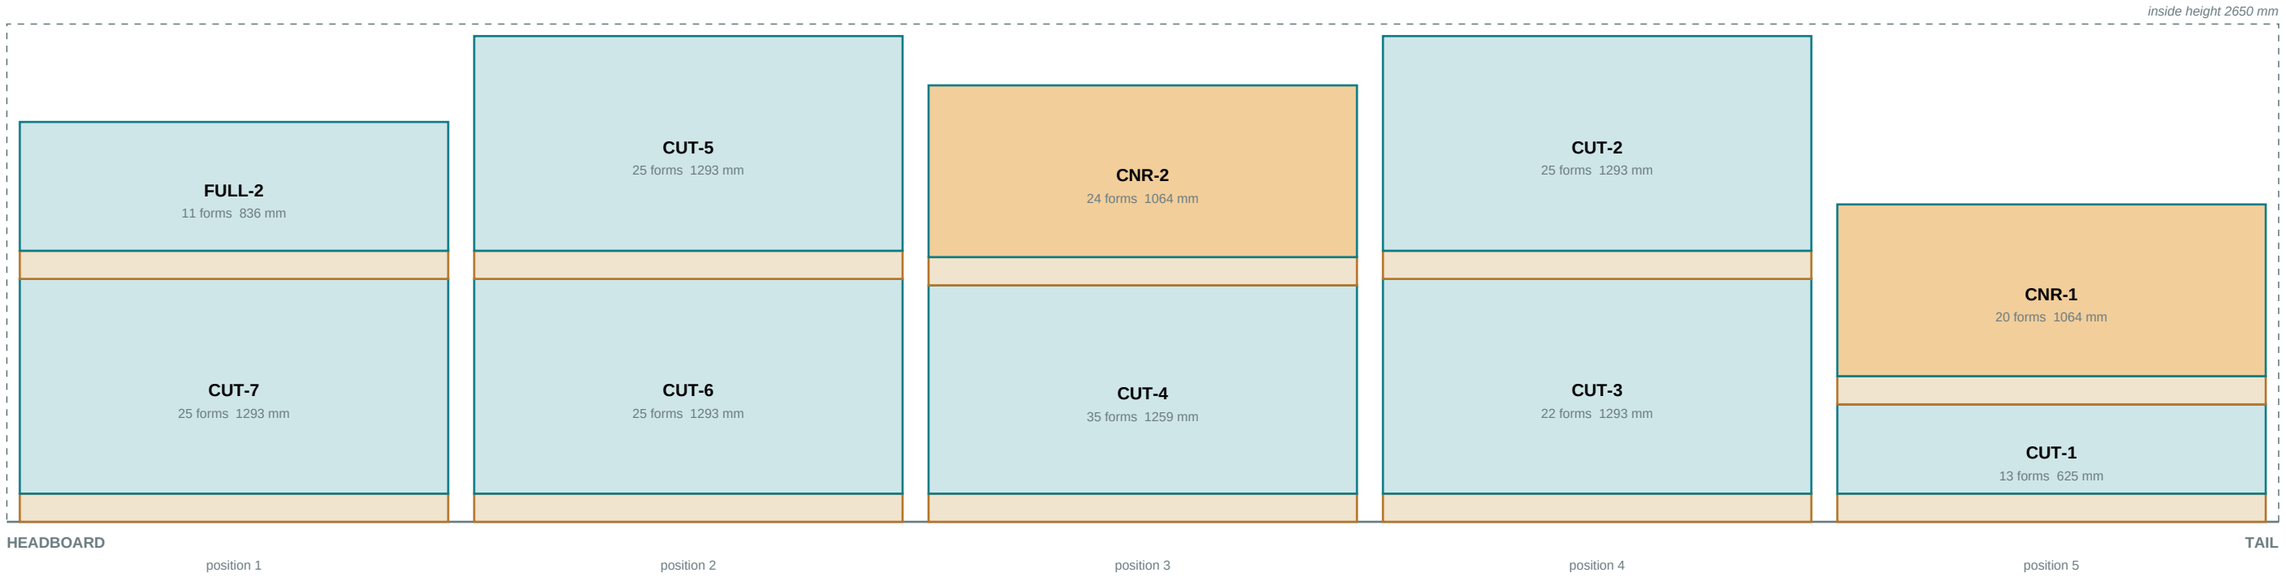

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. CNR-1 6in XR35 corners 20 forms courses FB courses 1-2
2. CUT-1 6in Std straights 13 forms courses FB courses 1-2
3. CUT-2 6in XR35 straights 25 forms courses FB courses 1-2
4. CUT-3 6in XR35 straights 22 forms courses FB courses 1-2
5. CNR-2 6in XR35 corners 24 forms courses L1 courses 1-3
6. CUT-4 6in Std straights 35 forms courses L1 courses 1-6
7. CUT-5 6in XR35 straights 25 forms courses L1 courses 1-6
8. CUT-6 6in XR35 straights 25 forms courses L1 courses 1-6
9. FULL-2 6in XR35 straights 11 forms courses L1 courses 1-6
10. CUT-7 6in XR35 straights 25 forms courses L1 courses 2-6

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-087 JAUS - Bromfelde Corner, London…	FORMS	225
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm

Delivery 1 - Load 2 of 2 - Artic 13.6 m

4 pallets in 2 of 5 floor positions | 63 forms | tallest column 2357 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

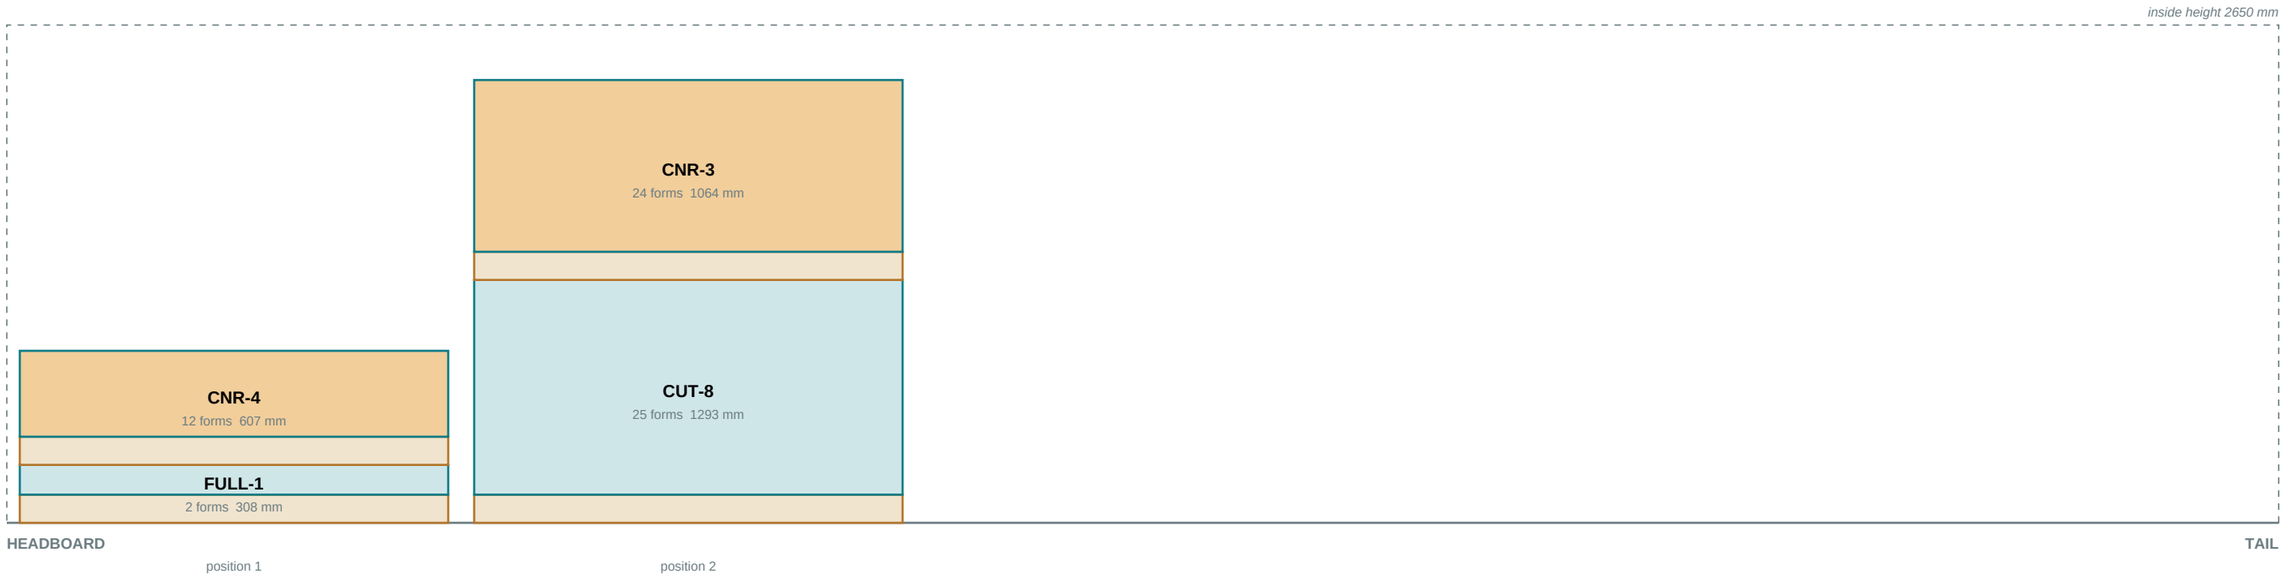

Unload order - 3 of 3 pallets come off out of build order, the price of stacking tallest forward

1. CNR-3 6in XR35 corners 24 forms courses L1 courses 3-5
2. CUT-8 6in XR35 straights 25 forms courses L1 courses 3-6
3. CNR-4 6in XR35 corners 12 forms courses L1 courses 5-6
4. FULL-1 6in Std straights 2 forms courses L1 course 6

Nudura™ **WAGON STACKING PLAN** **D1 LOAD 2**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-087 JAUS - Bromfelde Corner, London…	FORMS	63
VEHICLE	Artic 13.6 m	POSITIONS	2 of 5
PALLETS	4	TALLEST	2357 mm

Delivery 2 - Load 1 of 1 - Artic 13.6 m

9 pallets in 5 of 5 floor positions | 209 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

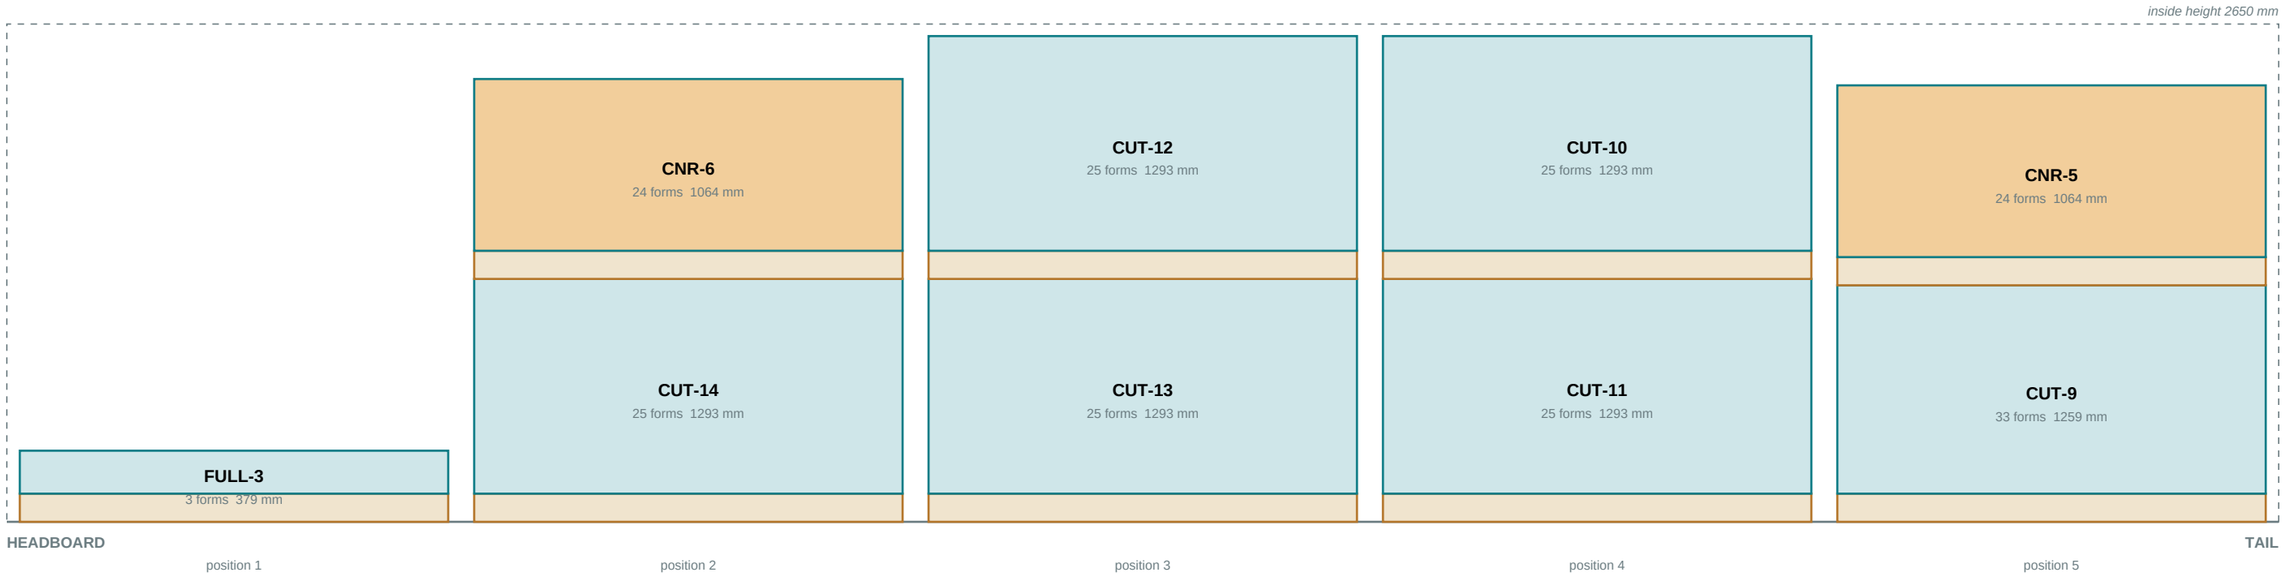

Unload order - 8 of 8 pallets come off out of build order, the price of stacking tallest forward

1. CNR-5 6in XR35 corners 24 forms courses L2 courses 1-3
2. CUT-9 6in Std straights 33 forms courses L2 courses 1-6
3. CUT-10 6in XR35 straights 25 forms courses L2 courses 1-6
4. CUT-11 6in XR35 straights 25 forms courses L2 courses 1-6
5. CUT-12 6in XR35 straights 25 forms courses L2 courses 2-6
6. CUT-13 6in XR35 straights 25 forms courses L2 courses 3-6
7. CNR-6 6in XR35 corners 24 forms courses L2 courses 4-6
8. CUT-14 6in XR35 straights 25 forms courses L2 courses 4-6
9. FULL-3 6in XR35 straights 3 forms courses L2 course 6

Nudura™ **WAGON STACKING PLAN** **D2 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-087 JAUS - Bromfelde Corner, London…	FORMS	209
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	9	TALLEST	2586 mm

Delivery 3 - Load 1 of 1 - Artic 13.6 m

10 pallets in 5 of 5 floor positions | 212 forms | tallest column 2586 mm of 2650 mm inside height

Column heights do not fall to the tail: unload order was kept, which the crew needs, and it conflicts with loading tallest-forward on this load.

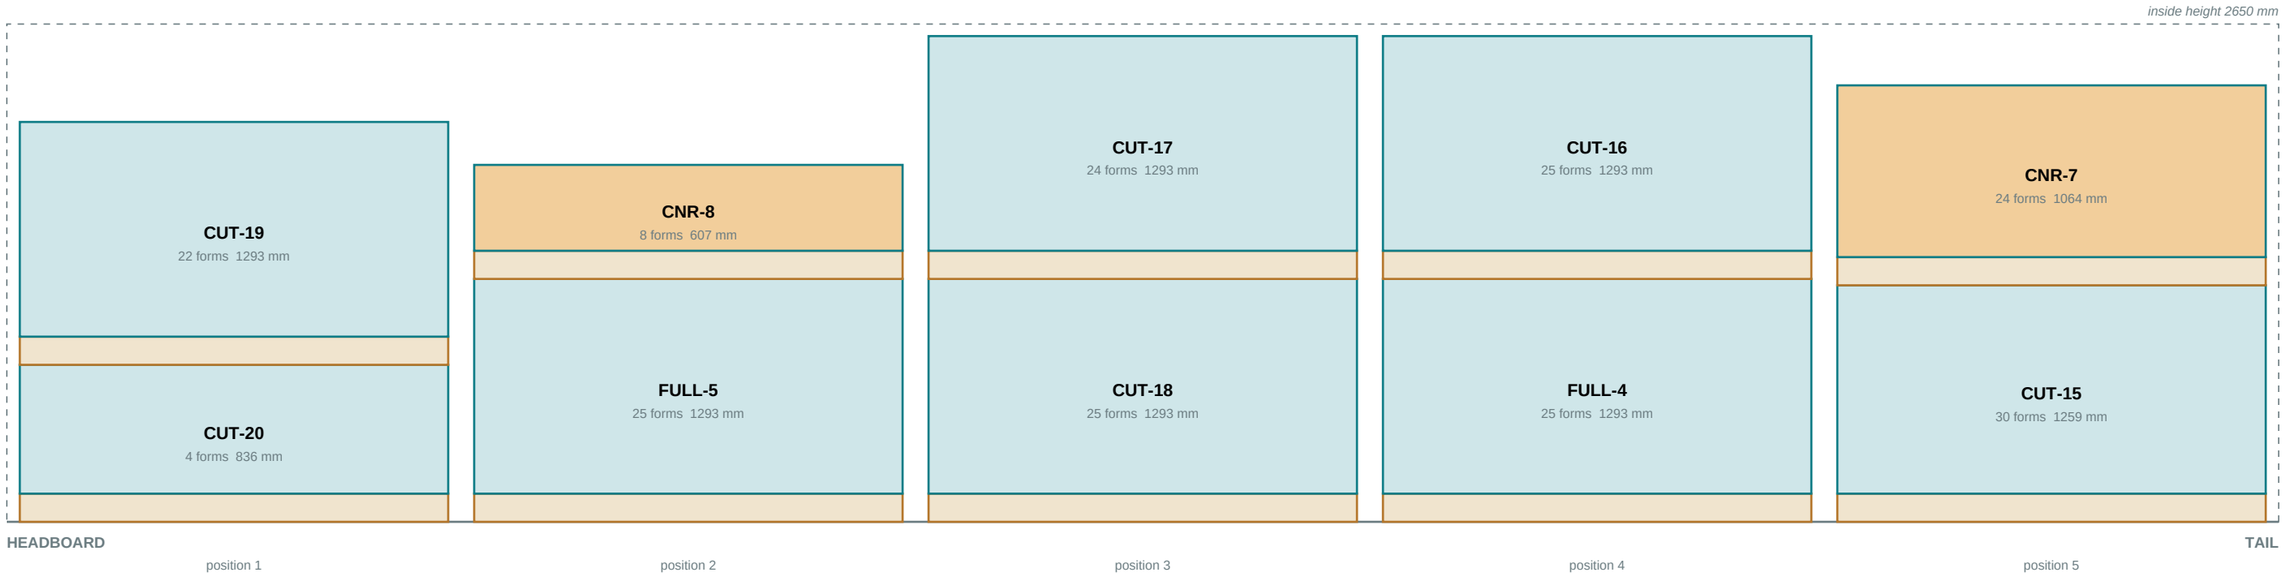

Unload order - 9 of 9 pallets come off out of build order, the price of stacking tallest forward

1. CNR-7 6in XR35 corners 24 forms courses L3 courses 1-6
2. CUT-15 6in Std straights 30 forms courses L3 courses 1-6
3. CUT-16 6in XR35 straights 25 forms courses L3 courses 1-6
4. FULL-4 6in XR35 straights 25 forms courses L3 courses 1-6
5. CUT-17 6in XR35 straights 24 forms courses L3 courses 2-6
6. CUT-18 6in XR35 straights 25 forms courses L3 courses 4-6
7. CNR-8 6in XR35 corners 8 forms courses L4 courses 1-2
8. FULL-5 6in XR35 straights 25 forms courses L4 courses 1, 2, 4
9. CUT-19 6in XR35 straights 22 forms courses L4 courses 1, 2, 3, 4, 5, 7, 8, 9
10. CUT-20 6in XR35 straights 4 forms courses L4 courses 4, 5, 6, 8, 9

Nudura™ **WAGON STACKING PLAN** **D3 LOAD 1**

Tallest column at the headboard; last needed on the floor

PROJECT	ES26-087 JAUS - Bromfelde Corner, London…	FORMS	212
VEHICLE	Artic 13.6 m	POSITIONS	5 of 5
PALLETS	10	TALLEST	2586 mm
